

**Minutes of the Executive meeting held on 31<sup>st</sup> December 2024 at Zilla Parishad Conference Hall under the Chairmanship of Collector & District Magistrate cum Chairman, District Mineral Foundation, Keonjhar**

---

The Executive Committee meeting was convened on 31<sup>st</sup> December 2024 at 11:00 AM, under the chairmanship of the Collector cum Chairman and Managing Trustee of DMF, Keonjhar, to review the progress of the projects implemented across various departments utilizing DMF fund.

The topics of discussions were as follows:

1. Department wise Project Status
2. DMF Perspective Plan
3. Audit and Annual Report of DMF
4. List of Projects to be approved under DMF
5. Other matter with permission of the Chair

The meeting was attended by the following officials (Attendance at Annexure II):

- Divisional Forest Officer (DFO), Keonjhar
- Divisional Forest Officer (DFO), Anandpur
- Deputy Director Mines (DD), Keonjhar Division
- Deputy Director Mines (DD), Joda Division
- Chief District Medical & Public Health Officer (CDM&PHO), Keonjhar
- DSDEO, Keonjhar
- Superintending Engineer (S.E), R&B, Keonjhar Division
- Superintending Engineer (S.E), R&B, Ghatgaon Division
- Superintending Engineer (S.E), RWD-I Division
- Superintending Engineer (S.E), RWD-II Division
- AEE, RWD, Anandapur Division
- Superintending Engineer (S.E), RWSS, Keonjhar Division
- Superintending Engineer (S.E), RWSS, Anandpur Division
- Land Acquisition Officer (LAO), Keonjhar &
- Members of PMU DMF

Following formal introductions by all the members present at the meeting, the Chair directed the members of the PMU, DMF, to present the status of the projects. The discussions are summarized as follows:

#### **1. Department wise Project Status**

At the outset, the members of the PMU, DMF, presented an overview of the submission status for the Gram Sabha, Utilization Certificates, and Completion Certificates pertaining to the projects of the Executive Committee members. Additionally, the delayed projects each exceeding 5 Crores, along with those ranging from 1 to 5 Crores, were thoroughly discussed, highlighting the hindrances involved in the projects. The discussions as department wise are summarized as follows:

a) R&B, Keonjhar Division:

- The SE, R&B Keonjhar Division provided an explanation for the delay in the "Bileipada to Nuamundi via Murgamahadev" project, stating that the Gram sabha has been unsuccessful on four occasions. The LAO, Keonjhar, has committed to conduct the Gram sabha one final time. If it remains unsuccessful in securing the approval for the remaining 700 meters, the project will be considered for closure.
- The project "Construction of a 200 seated Boys Hostel at Govt ITI Barbil, Keonjhar," which was sanctioned in 2023 from DMF, has not yet commenced. The SE, R&B, Keonjhar, explained that the tender process has been non-responsive for two times. As a result, the tender process has now been initiated for the third time.
- The project "Construction of Skill Development Training Centre at Telkoi in Keonjhar district" sanctioned on 17.10.2023 for the year 2023-24, has had an agreement finalized with the successful bidder as per SE, R&B Division, Keonjhar and the work is expected to commence soon.
- The SE mentioned that proposal has been submitted to DMF for the improvement of Suakati – Dubuna road from Ch 3/400 to 31/400 Km for renewal coat tune the amount of Rs 9.00 Cr for sanction of funds out of DMF. The proposal was approved under 11 TB as well.

Directions from the Chair:

- The Chair instructed the SE, R&B Division, Keonjhar, to accelerate the progress of the delayed projects and work towards their prompt completion. Additionally, the Chair directed the LAO, Keonjhar, to coordinate on land acquisition issues and address any other hindrances hindering the progress of these projects.
- On the proposal of Suakati – Dubuna road the Chair mentioned that being the recurring nature of work of renewal coat and looking at the cost, the PMU team may take a joint visit with concerned stakeholders to assess the actual need.

b) R&B, Ghatagaon Division:

- The road widening for the project "Improvement of Sailong - Brahmanipal - Khaliamenta" has been delayed due to local obstacles. Additionally, the dismantling of staff quarter is required, as stated by the SE, R&B, Ghatagaon Division. The S.E has been in communication with the Tehsildar, Ghasipura, to resolve the land dispute issues affecting the project in order to complete the project at the earliest.
- The SE, R&B, Ghatagaon, explained that for the project "Mareigaon Chowk to Soso via Dhenka Road," he has communicated with the Tehsildar, Hatadihi to address the land related issues and ensure the completion of the project by end of February month.
- SE, R&B, Ghatagaon mentioned that the construction of Block Level Library in few sites are almost completed and the user department to be finalized soon in order to apply for the metering connection for completion of the electrical work.

Directions from the Chair:

- The Chair instructed the SE, R&B Division, Ghatagaon, to accelerate the progress of the delayed projects and work towards their prompt completion. Additionally, the Chair instructed S.E to coordinate with Tehsildar, Ghasipura and Hatadihi to resolve the pending issues involved in the above projects. He further mentioned that for the Block Level Library the modalities will be finalized very soon in order to resolve the issues.

c) RWD, I and II, Keonjhar Division:



- The SE, RWD-I Division, explained that the delay in the project "Improvement of Road from Machhakandana Nallah to Kadagarh via Dhatika" has been caused by a shortage of materials and sand near the project site. He has committed to resolve these issues and ensuring the project will be completed by 31st March 2025.
- The members of the PMU, DMF, presented a list of unconnected habitation projects in the Banspal and Telkoi blocks, which have been pending for technical sanction at the Chief Engineer Office, RWD, Bhubaneswar for a long time.
- S.E, RWD-II Division, Keonjhar mentioned that the project "Improvement of road from Rugudi to Kalmang road" is getting delayed by the hindrances caused due to traffic diversion by the public. SE has committed to complete the project by 31st May 2025.
- Construction of Bridge over local Nallah on Phuljhar to Dhaladihi road: For this project S.E, RWD-II has committed to finish the project by 30th June 2025.

d) RWD, Anandpur Division:

- The members of the PMU, DMF, presented a list of unconnected habitation projects in the Harichandanpur block (Pg 25 of Annexure I), which have been pending for technical sanction at the Chief Engineer Office, RWD, Bhubaneswar and the list of projects which are in tender stage waiting for the agreement to be drawn. For the above list of projects, the division officials have committed to expedite the progress of the projects.
- Construction of Dimiria to Jambhara via Dhaipokhari road from 0/000 km to 4/500 km: For this project, revised estimate has been submitted to CE office for approval and project timeline for completion as committed by SE, RWD, Anandpur was 31.03.2025.
- Construction of road from Purunapani to Chakaamaba sahi from 2/600 to 3/300 km: The SDO, RWD, Anandpur Div., informed the Chair that the road falls within the Tiger Corridor under the authority of the DFO, Anandpur. As per DFO, Anandpur, it was not intimated to him from RWD, Anandpur division earlier. He assured that a letter would be sent to the DFO to intimate for necessary action for the timely completion of the project.
- Improvement of road from Khajuria Pancham to Dangadhar: Due to change in scope, deviation and forest diversion issues the project was hindered initially. Further, RWD, Anandpur division has committed to complete the project by 31st May 2025.

Directions from the Chair:

- The Chair instructed the SE, RWD-I, II and Anandpur division to expedite the unconnected habitation projects in the Banspal, Telkoi and Harichandanpur Blocks. Also, he instructed the SEs of respective departments to adhere to the stipulated timelines of completion for the list of projects above 5 Crore and the list of projects ranging from 1 to 5 Crore (Annexure I).
- The Chair also instructed the divisions to take necessary follow ups for the clearance of road proposals from Chief Engineer Office, RWD, Bhubaneswar at the earliest.

e) RWSS, Keonjhar and Anandpur Division

- Piped Water Supply (PWS) to Mining affected villages of Champua, Jhumpura, Keonjhar and Banspal Block - 589 Villages: For the above projects, SE, RWSS, Keonjhar elaborated that after joint verification with SE, R&B, Keonjhar the Pipeline restoration is under progress and revised estimates for restoration of pipeline to be submitted by 5th January 2025.<sup>1</sup>

<sup>1</sup> Annexure -1, Presentation-slideno.17

- Additionally, he mentioned that out of 388 pipeline intersection locations, 149 have been temporarily shifted against the damaged pipelines by Kanupur Irrigation Project division. Furthermore, the number of intersection points has increased from the previously reported 388 to 457. As per SE, RWSS, Keonjhar the Joint verification report along with design data have been submitted and revised estimate has been sent to E.I.C office RWSS, BBSR on 26.12.2024 towards restoration of damaged pipelines.
- He further requested the Chair to intervene and direct the stakeholders involved in the mentioned projects such as R&B Divisions, RW Divisions, TPNODL, Kanupur Irrigation Project Division and agencies like JSW and JSPL—to submit a detailed work plan prior to project execution which would aim to prevent delays due to the damaged pipelines while laying and restoration of pipelines in the above project.

Directions from the Chair:

- The Chair instructed the SE, RWSS, Keonjhar and Anandpur division to expedite the activities Mega PWS projects. Also, he instructed the SEs of respective departments to adhere to the stipulated timelines of completion for the list of projects above 5 Crore and the list of projects ranging from 1 to 5 Crore (Annexure I).
- He further mentioned that both the division to prepare the As-Builts simultaneously and keep the updated map ready for periodic meetings. The final As-Builts must be reviewed once with the concerned stakeholders before closure of the project.

f) CDM & PHO, Keonjhar

- The DMF-PMU team presented agenda points regarding the implementation of projects under CDM&PHO, Keonjhar.
- CDM&PHO, Keonjhar notified that the identification of locations for 34 digital dispensaries had been completed, and the implementation of these dispensaries would commence shortly. The PMU team suggested that reports from Mission Antodaya (2022), which highlighted infrastructural gaps, has been mapped, which could be utilized to position these additional digital dispensaries more effectively. Also, the route map of the MMUs in the district may also be changed accordingly as per the ground need for better inter relation of services.
- CDM&PHO, Keonjhar mentioned that compliance for doctors hired under DMF had been achieved, with only a few cases where agreements were yet to be submitted. Additionally, CDM&PHO, Keonjhar emphasized that the age limit for doctors should be restricted to 70 years and existing doctors working beyond this age limit, their agreement may not be renewed, considering that physical and cognitive capabilities declines with age, which could impact the quality of patient care and the doctor's ability to meet the demanding requirements of their roles effectively. This is in line with the revision of maximum age for appointment of doctors on contractual basis vide Government in Health &FW Deptt. Resolution no.22396/H dated 06.09.2019. The PMU team highlighted that for the monitoring of attendance of Doctors in the District, an app-based attendance system with geo-fencing was repeatedly recommended for implementation to the CDMO team but it has not been implemented so far. They reiterated that this approach would be more practical and effective than biometric systems for ensuring accountability.
- CDM&PHO, Keonjhar reported facing challenges with the GeM portal, which had caused delays in the procurement of thalassemia diagnostic machines. However, they assured that the necessary procurement processes would be expedited and completed at the earliest



opportunity. The PMU team suggested that the timely acquisition of this diagnostic machine was critical for the early detection and effective management of thalassemia.

- CDM&PHO, Keonjhar stated that there were no issues or objections regarding the transfer of administrative and financial control to Dean & Principal, DDMCH for the ministerial staff and paramedics hired through an outsourcing agency and working at DDMCH, Keonjhar. The PMU team suggested that the transfer could be executed by incorporating an addendum to the agreement if needed, which would include DDMCH, Keonjhar as a third party, in addition to the existing parties, CDM&PHO, Keonjhar, and the outsourcing agency.
- CDM&PHO, Keonjhar highlighted the challenge of managing multiple ongoing DMF projects due to the absence of dedicated support staff for DMF-related tasks, including project oversight, monitoring, and field visits. Given the substantial number of projects being implemented, there was a recognized need to strengthen the office of CDM&PHO to ensure efficient execution, supervision, and monitoring of DMF projects.

#### Directions from the Chair:

- The Chair directed CDM&PHO, Keonjhar to effectively plan for the identification of appropriate locations for the new digital dispensaries as per the t&c of the agreement in order to ensure proper utilization of resources and address infrastructural gaps effectively.
- The Chair expressed his displeasure and directed CDM&PHO, Keonjhar to submit the compliance at the earliest pertaining to the PAR/Agreement of the doctors and implement an app-based attendance system. The PMU team was directed to facilitate this process and ensure its smooth and timely implementation. The Chair suggested the PMU team to check the attendance system used by the DFO office, which includes more comprehensive parameters. He also suggested that this system, with geo-fencing, be implemented immediately to ensure effective monitoring and accountability of the doctors. Additionally, the Chair directed CDM&PHO, Keonjhar to assess the overall requirement of doctors at PHC, CHC, SDH, and DHH and submit the report to DMF. Furthermore, the Chair directed CDM&PHO, Keonjhar to implement the discussed age criteria of the doctors following due process.
- The Chair expressed concerns over the delay in procuring the thalassemia diagnostic machine and directed CDM&PHO, Keonjhar that the procurement process be expedited without further delay. The chair emphasized the importance of ensuring that the necessary equipment is in place as soon as possible to support the timely diagnosis and treatment of thalassemia.
- The Chair directed CDM&PHO, Keonjhar to execute the transfer of administrative and financial control to Dean & Principal, DDMCH for the ministerial staff and paramedics hired through an outsourcing agency and working at DDMCH, Keonjhar following due process.
- The Chair directed the CDM&PHO, Keonjhar to submit a proposal, following due process, for the engagement of two nos. of dedicated support staff for DMF projects. These resources could be hired through an outsourced agency. Furthermore, the Chair emphasized the need for prompt implementation of this arrangement to ensure the smooth execution of DMF projects, with the budget for these resources being routed through the contingency fund of the DMF projects under CDM&PHO.

#### g) Divisional Forest Officer (DFO), Keonjhar

- The DFO Keonjhar mentioned that his office has been implementing several plantation projects out of DMF funds and in order to effectively do the activities w.r.t. seasonal timelines, sometimes the funds were utilized as per priority within the listed components of the project. The office has

also intimated the same during submission of MPRs and has submitted the UCs accordingly and therefore the subsequent tranches as per requisition may be processed further.

Directions from the Chair:

- The Chair upon listening the above has reiterated that such prioritization of components may be needed for successful implementation of the plantation activities and directed the PMU team to process the requisitions following due process.

## 2. DMF Perspective Plan

The members of PMU-DMF presented the points regarding next 5 years Perspective plan of DMF to the Chair which are as follows:

- **Identification of Directly and Indirectly affected villages:** Deputy Director of Mines (Keonjhar/Joda) need to provide the geographical coordinates of mining areas, along with a list of villages and Gram Panchayats (GPs) located within 15 km radius from the mines or cluster of mines for directly affected and 25 km radius from the mines or cluster of mines for Indirectly affected beyond the directly affected area (as per the revised guidelines of PMKKKY – Jan 2024). DDM (Keonjhar/Joda) may send the updated list to Odisha Remote Sensing and Application Centre (ORSAC) for further vetting and verification. A communication in this regard was also shared to DDM (Keonjhar/Joda) for initiating the process at the earliest.
- Secondary datasets such as Mission Antyodaya- 2022, NFHS-2019, UDISE, Keonjhar Master Plan, etc may be referred for conducting a gap analysis in the affected regions.
- Organizing consultations with key stakeholders to ensure alignment and effectiveness of proposed interventions.

Directions from the Chair:

- The Chair directed DDM Keonjhar/Joda to initiate the necessary process as briefed above. Further the Chair mentioned that the preparation of DMF perspective plan is an important exercise and the same will also lay the foundation for year wise action plan indicating sector wise plan and asked all the members to provide necessary support in this regard.

## 3. Audit and Annual Report of DMF

The members of PMU-DMF presented the following points to the Chair:

- The Audit report for FY 2022-23 has been prepared by the Chartered Accountant (CA) and uploaded to the DMF Portal. Post facto approval will be sought in the upcoming Trust Board meeting.
- The Tax audit report for FY 2023-24 was submitted to the Income Tax Department within the stipulated time.
- The Annual reports for FY 2022-23 and FY 2023-24 will be approved in the upcoming Trust Board meeting.

## 4. List of Projects to be approved under DMF

As per proposal of concerned line departments and other subjects, the list of projects (36 nos.) to be approved has been placed for the perusal of the committee (pg. 41 to 46 of Annexure I). After deliberations, the list of the projects was approved by the Executive Committee. Further, Collector requested all the line departments to submit the project proposals in anticipation of the upcoming Trust Board following ODMF rules at the earliest.



## 5. Other matters

The Chair after listening to the above discussions also mentioned that:

- As apprised by the members, looking at the quantum of the DMF works across sectors (a major part in Infrastructure) and work load of the existing line departments suitable PSUs may be entrusted with the work following due process.
- Line Departments to mandatorily conduct Gram Sabha before execution of the projects as specified in the ODMF rules and to submit the utilization and completion certificates in time bound manner.
- DDMs to ensure immediate validation of major mineral collection figures as per follow up meetings and directions of P&C Department to fill the gaps.
- Line departments to close the DMF portal entry of the projects in next 1 week's time.
- Change of project site must be avoided by the departments and the same must be diligently checked while preparation of the DPR. Proper documentary proofs to be maintained at the level of Line departments during execution of work.

At the end, the Chair emphasized the need for all line departments to expedite the delayed projects. Additionally, the Chair instructed PMU-DMF to closely monitor and follow up on the tasks mentioned above to ensure timely resolution of pending activities raised by the line departments and to meet the project deadlines.

The meeting ended with a vote of thanks to the Chair.

  
Collector-cum-Chairperson,  
DMF, Keonjhar

Memo No. 1113/DMF.

DATE: 28.03.2025

Copy forwarded to DFO, Keonjhar / DFO, Anandpur / DDM, Keonjhar / DDM, Joda / SE, R&B Division, Keonjhar / SE, R&B Division, Ghatagaon / SE, RWD-I, Keonjhar / SE, RWD-II, Keonjhar / SE, RWD Anandapur / SE, RWS&S, Keonjhar / SE, RWS&S, Anandapur / CDM&PHO, Keonjhar / DSDEO, Keonjhar / LAO, Keonjhar for information and necessary action

  
Collector-cum-Chairperson,  
DMF, Keonjhar.



(Annexure I)



Review on

# **Status of Projects**

## **Executive Committee Meeting**

### **District Mineral Foundation, Keonjhar**

Date: 31<sup>st</sup> December 2024

## INDEX

S. No.	Content	Slide No
1	Department wise Project Status	<u>07</u> to <u>31</u>
2	DMF Perspective Plan	<u>32</u> to <u>39</u>
3	Audit and Annual Report of DMF	<u>40</u>
4	List of Projects to be approved under DMF	41 to 46
5	Other Matter with permission of the Chair	

## Abstract of Gramsabha / UC / Completion certificate

Sl. No.	Name of the Department	No. of Project	Pending of Gram Sabha (Nos.)	Sanction Amount (Cr.)	Release Amount (Cr.)	UC Submitted (%) w.r.t Release amt.	Completion Certificate Submitted	Agreement Copy to be Submitted	Remarks
1	EE R& B Keonjhar	153	143	1400.33	960.34	89.61%	75	71	
2	EE R&B Ghatagoan	57	55	285.09	155.22	77.90%	15	38	
3	EE RWD Anandapur	183	150	525.31	185.53	70.81%	53	51	
4	EE RWD-I Keonjhar	18	13	30.45	22.16	92.23%	09	03	
5	EE RWD-II Keonjhar	166	152	647.43	222.72	77.69%	24	75	
6	DFO, Anandapur	06	04	4.61	2.82	91.57%	63	56	
7	DFO, Keonjhar	10	06	14.29	5.26	87.69%	03	09	01 project related to works
8	RWSS Keonjhar	127	02	825.65	714.42	97.49%	99	92	
9	RWSS Anandapur	33	06	550.52	462.12	77.70%	29	33	



## Slide 3

SB0

[@Preetam Karmakar] ...ranjit s  
Swagat Bisoyi, 2024-12-26T11:33:30.112

## Abstract of Ongoing / Not started Projects (Major Infra > 5cr)

Executing department	Total (Ongoing + Not started for projects > 5cr )	Ongoing	Not started	Delayed
EE R& B Keonjhar	28	24	04	16
EE R&B Ghatagoan	08	05	03	05
EE RWD Anandapur	32	16	16	0
EE RWD-I Keonjhar	03	03	00	01
EE RWD-II Keonjhar	43	22	21	08
DFO Keonjhar	01	01	00	01
RWSS Anandapur	03	03	00	03
RWSS Keonjhar	03	03	00	02
<b>Grand Total</b>	<b>121</b>	<b>77</b>	<b>44</b>	<b>36</b>

# Abstract



Keonjhar

₹ 12,266.6 + Crs

Total DMF Funds

₹ 9,814.84 + Crs

Total Fund Sanctioned

3,271 +

Total Project Sanctioned

968  
Completed


1,618  
On-Going

683  
Not-Started

2  
Closed



Fund Accrual vs Spending (Crs)

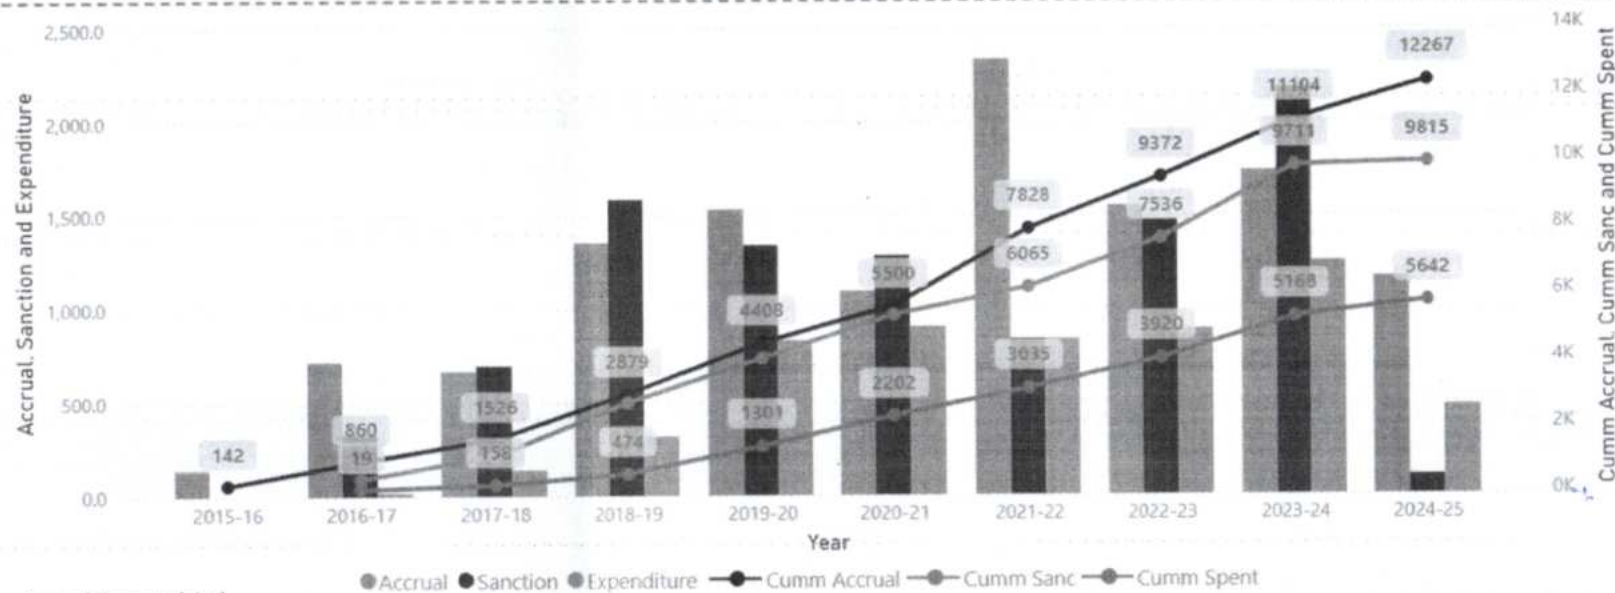

Accrual Data Updated

(Up to Nov. 2024)

80.0 %

Sanctioned


57.5 %

Released


PBI



## Abstract – Sector Wise Allocation

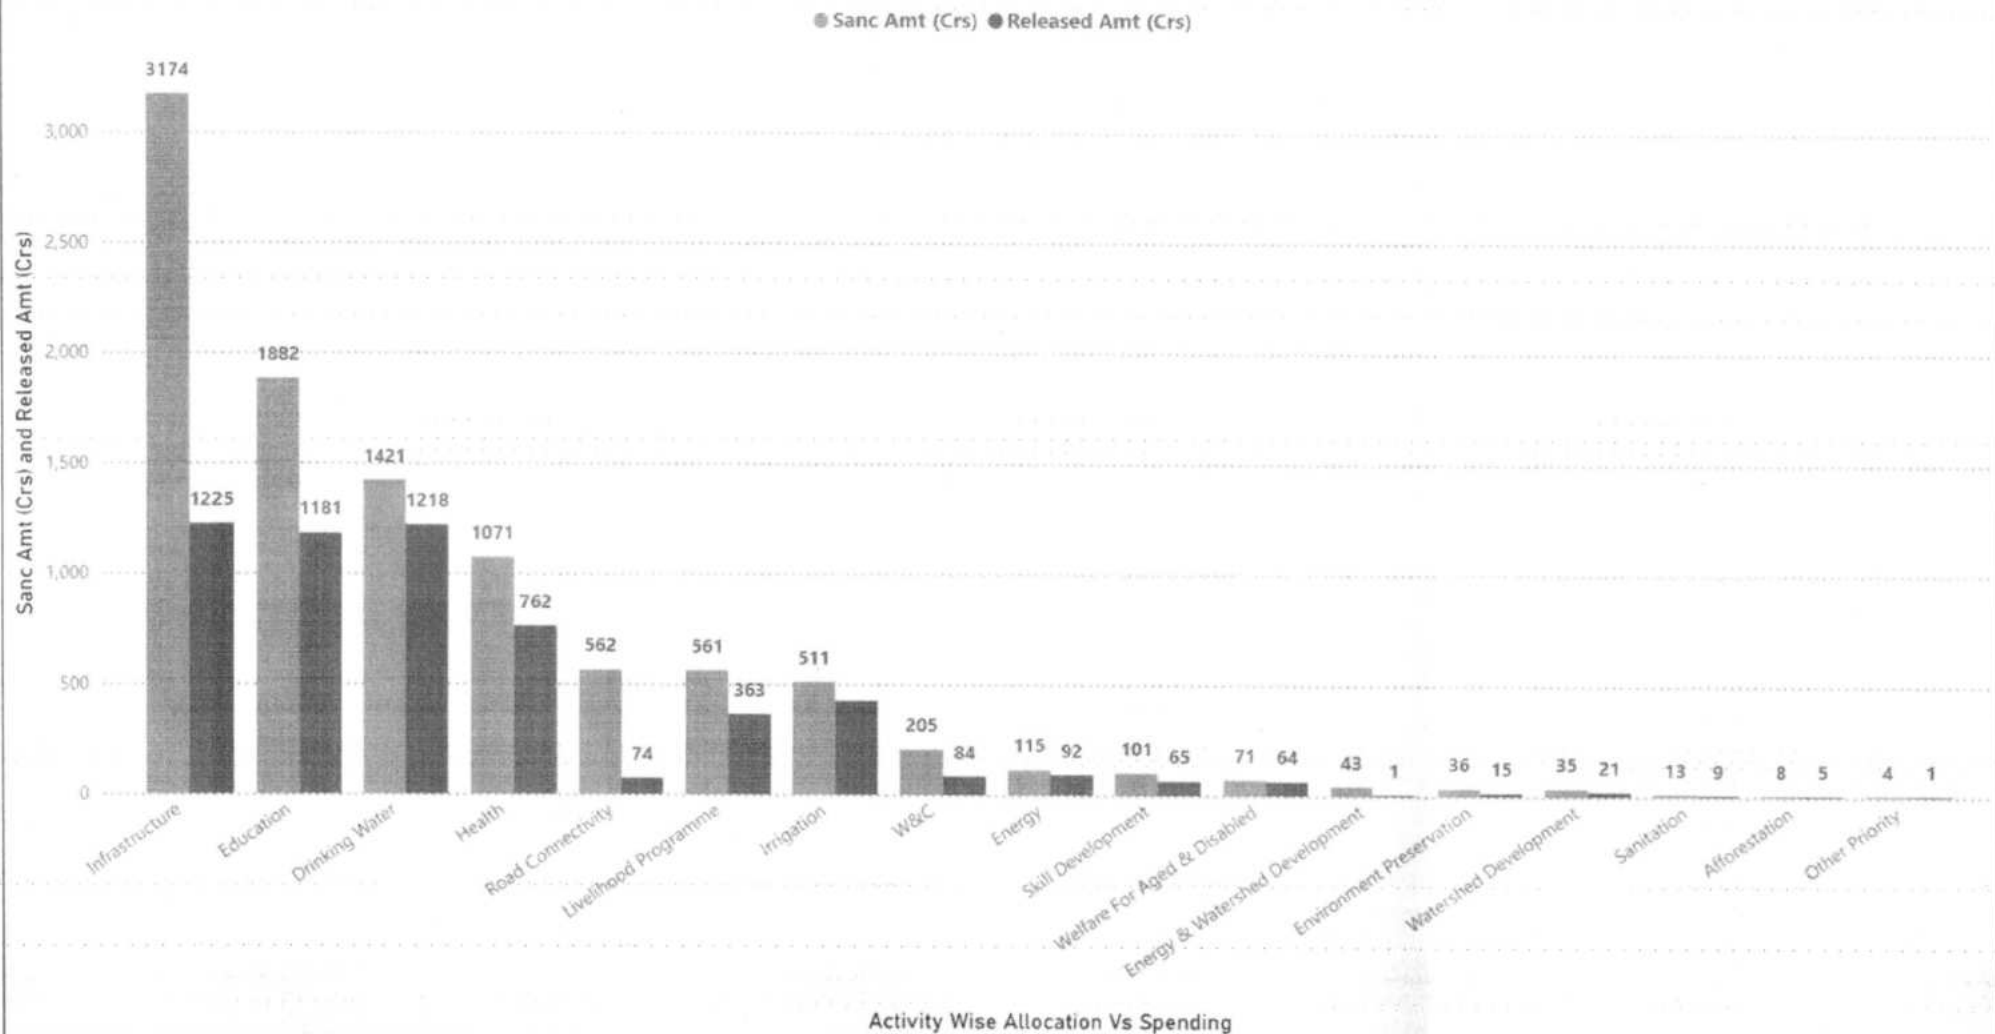

# Abstract – Department Wise Allocation

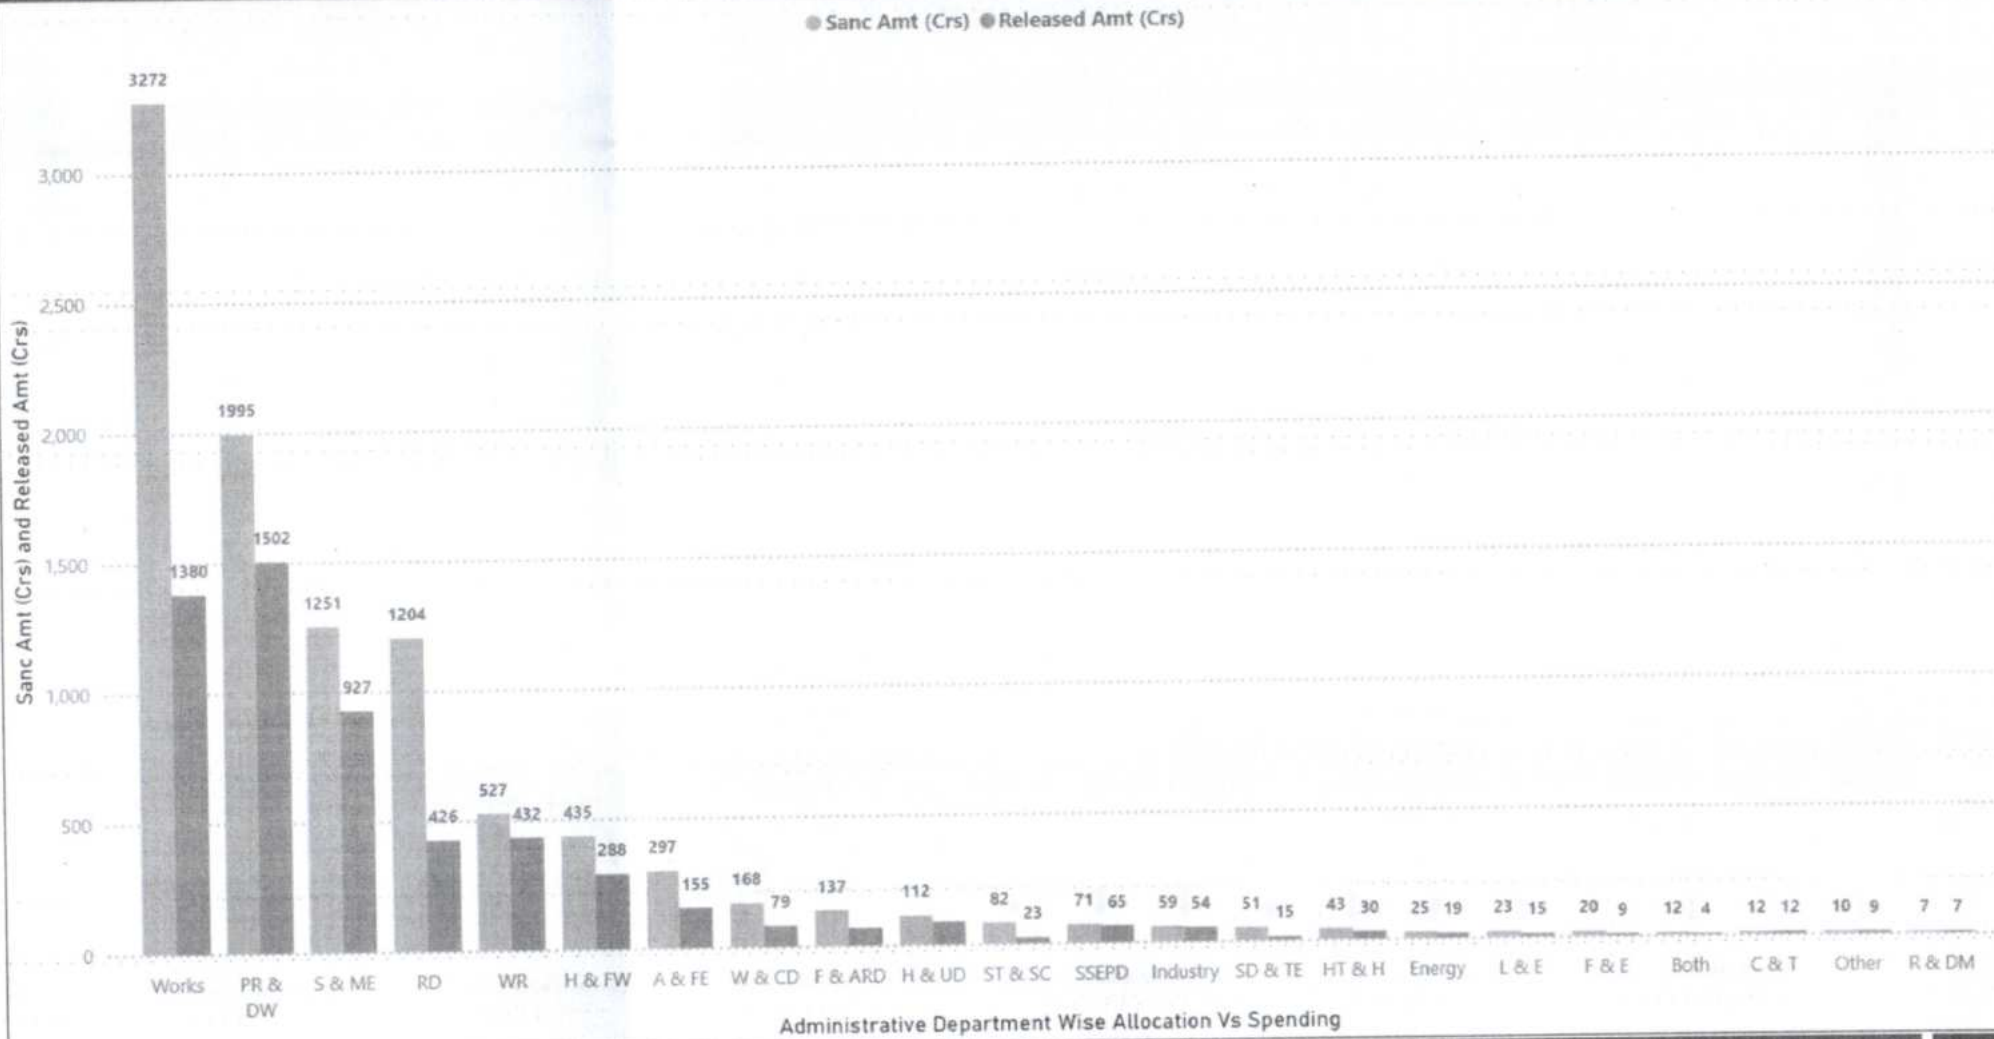

PBI


# R&B, Keonjhar Division



## Delayed Projects (Major Infra > 5cr)

**Bamebari to Ranasala Ghat via Joda from 4/800 Km. to 17/800 Km. of Joda - Bamebari Exp.way No. II.**




Sl. No	Project name	Sanctioned amount (in cr.)	Released amount (in cr.)	Delayed (in days)
1	Bamebari to Ranasala Ghat via Joda from 4/800 Km. to 17/800 Km. of Joda - Bamebari Exp.way No. II.	91.38 Sanction date 05.12.2017	80.33 (88% released)	4 years 9 months
2	HL bridge over Ardei river at Mananda connecting to Arsala Chauthia Road	13.95 Sanction date 21.11.2016	11.40 (82% released)	5 years 1 month
3	Bileipada-nuamundi via Murgamahadev road, 15 km	26.79 Sanction date 21.11.2016	23.75 (88% released)	5 Years 9 month
4	Const. of 200 seated Boys Hostel at Govt ITI Barbil, Keonjhar	9.99 Sanction Date 21.09.2023	00.00 (0% Released)	Not Started 1 Year

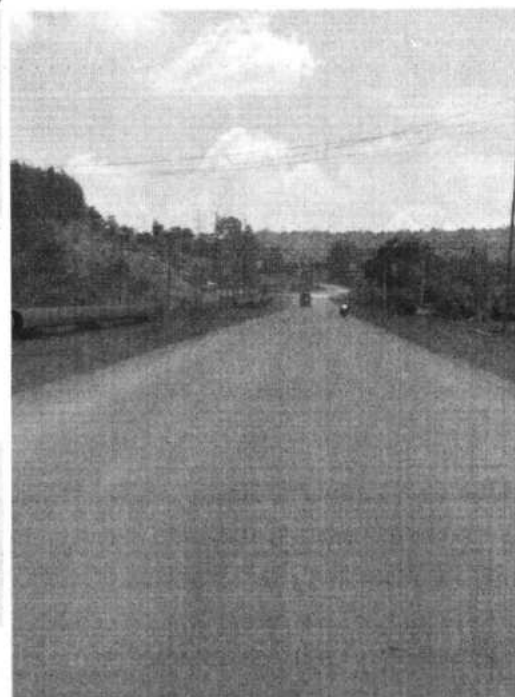

**Bileipada-nuamundi via Murgamahadev road**



**Approach Road at Mananda connecting to Arsala  
Chauthia Road**

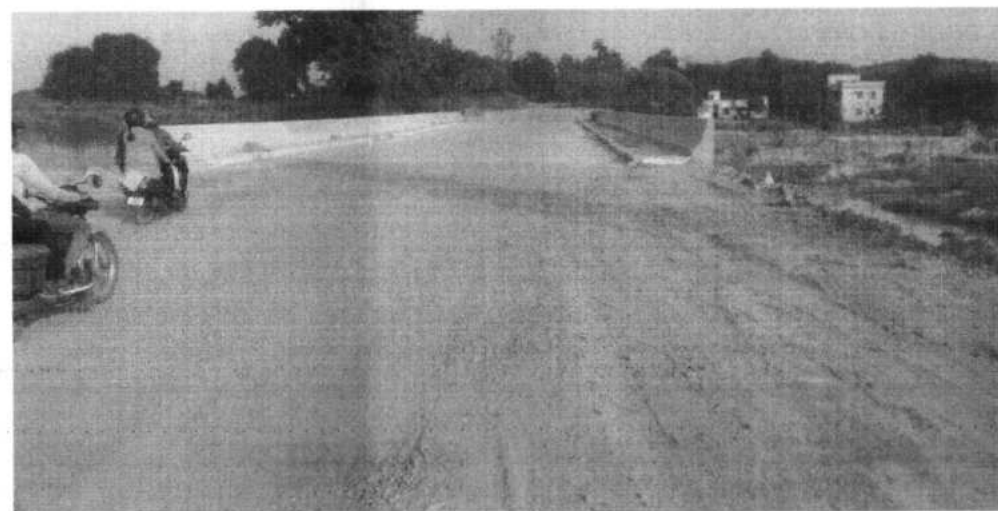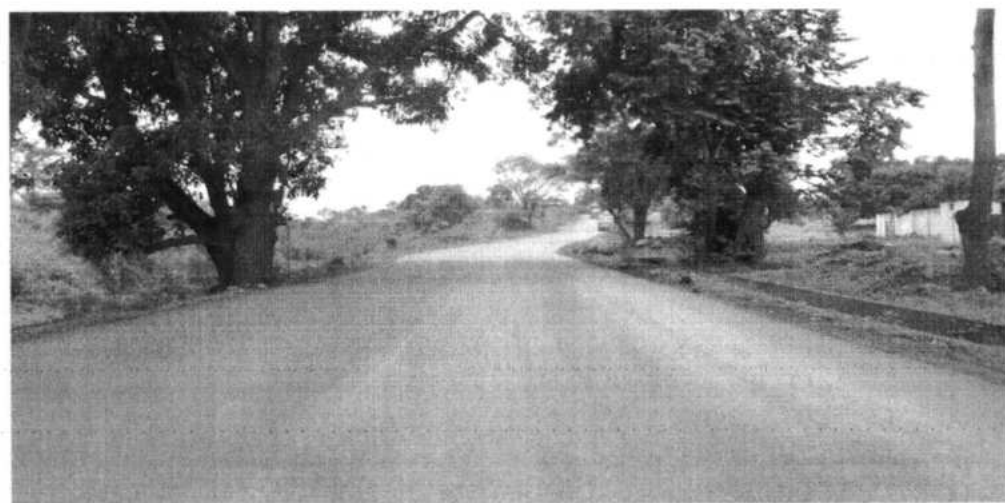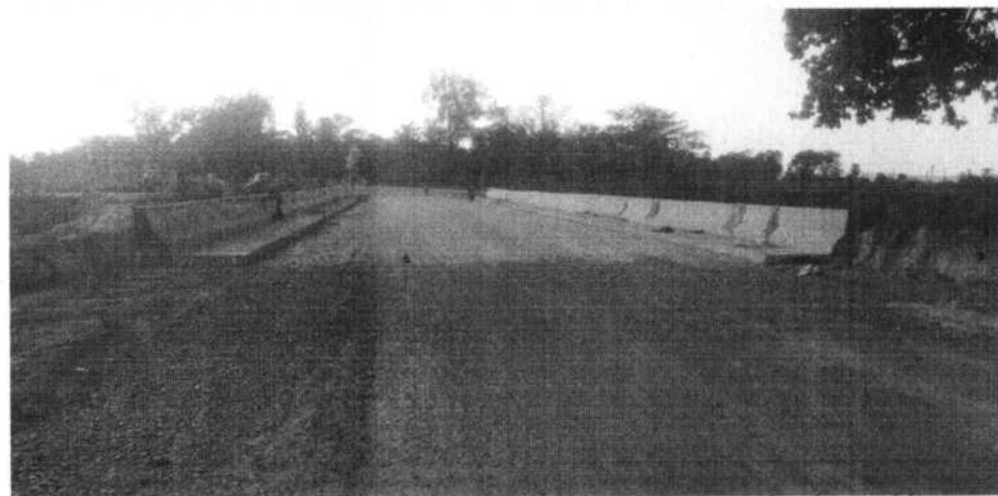


# R&B, Ghatagaon Division



## Ongoing Projects (Major Infra > 5cr)

Sl. No	Project name	Sanctioned amount (in cr.)	Released amount (in cr.)	Delayed (in days)
1	Improvement of Sailong Brahmanipal khaliamenta	<b>20.50</b> Sanction Date 22.11.21	<b>18.66</b> (91% released)	1 year 4 months
2	Mareigaon chowk to Soso via Dhenka road	<b>22.83</b> Sanction Date 22.11.21	<b>21.53</b> (94% released)	1 year 1 month
3	Harichandanpur to Daitari road (1/00 km to 16/00 km)	<b>34.10</b> Sanction Date 22.11.21	<b>23.87</b> (70% released)	1 year 1 month

## Improvement such as widening and strengthening to Harichandanpur to Daitari road

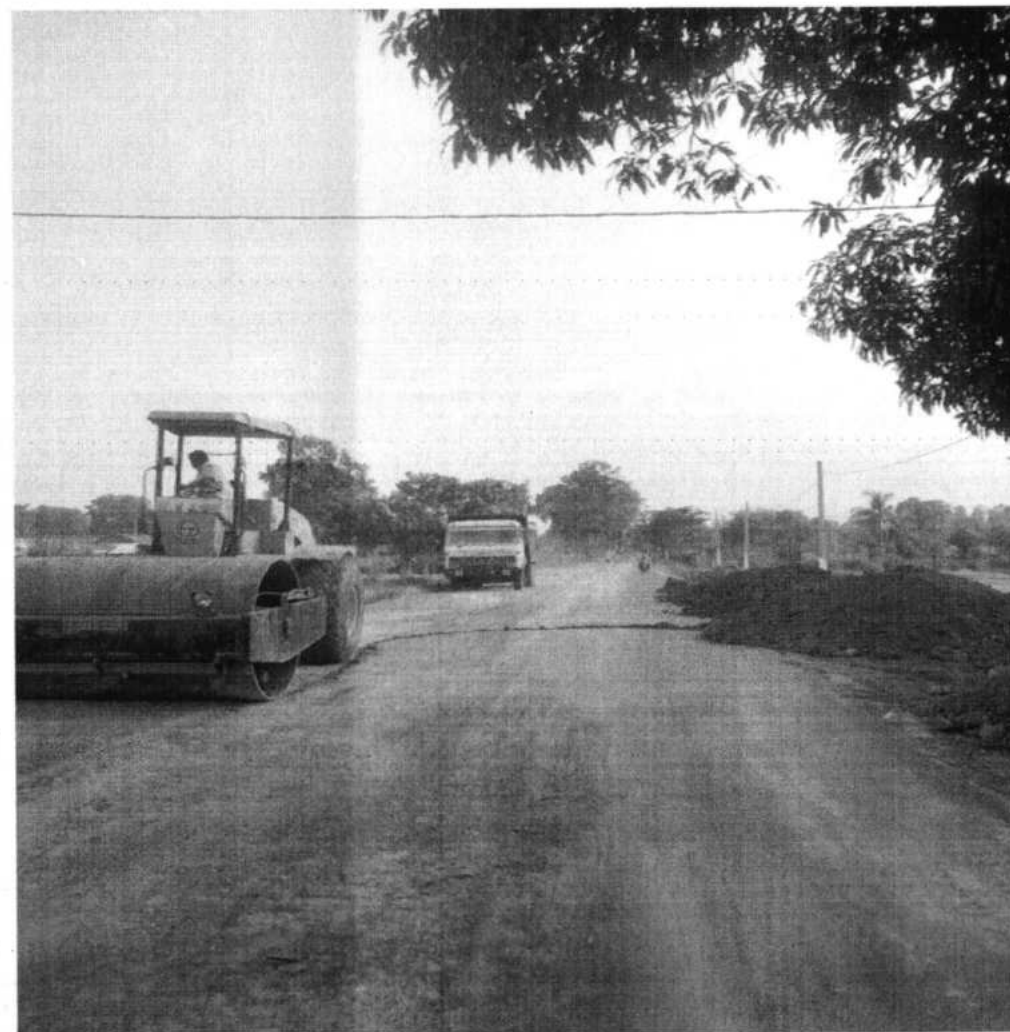

# R.W. Division – I & II, Keonjhar

## Delayed Projects (Major Infra > 5cr) RWD -II

Sl. No	Project name	Sanctioned amount(in cr.)	Released amount(in cr.)	Delayed (in days)
1	Impvt. Of road from Rugudi to Kalmang road	11.88 (Sanction dt : 25.11.20)	7.41 (60% released)	2 years 11 months
2	Const. of Bridge over local Nallah on Phuljhar to Dhaladihi road	7.07 (Sanction Dt : 23.12.21)	6.67 (94% released)	1 year 9 months

## Delayed Projects (Major Infra > 5cr) RWD -I

1	Improvement of road from Machhakandana Nallah to Kadagarh via Dhatika	5.49 (Sanction dt : 21.10.22)	5.26 (96% released)	1 year 5 months
---	---	----------------------------------	------------------------	-----------------

## Rugudi to Kalmang road






# R.W. Division, Anandapur

## Projects (Major Infra > 5cr) RWD -Anandapur

Sl. No	Project name	Sanctioned amount (in cr.)	Released amount (in cr.)	Delayed (in days)
1	Impvt. Of road from Khajuria Pancham to Dangadhar	6.21 Sanction Date 10.08.21	1.86	Ongoing (1 year)
2	Const. of Dimiria to Jambhara via Dhaipokhari road from 0/000 km to 4/500 km	6.92 Sanction Date 14.12.22		9 months

### Improvement Of road from Khajuria Pancham to Dangadhar

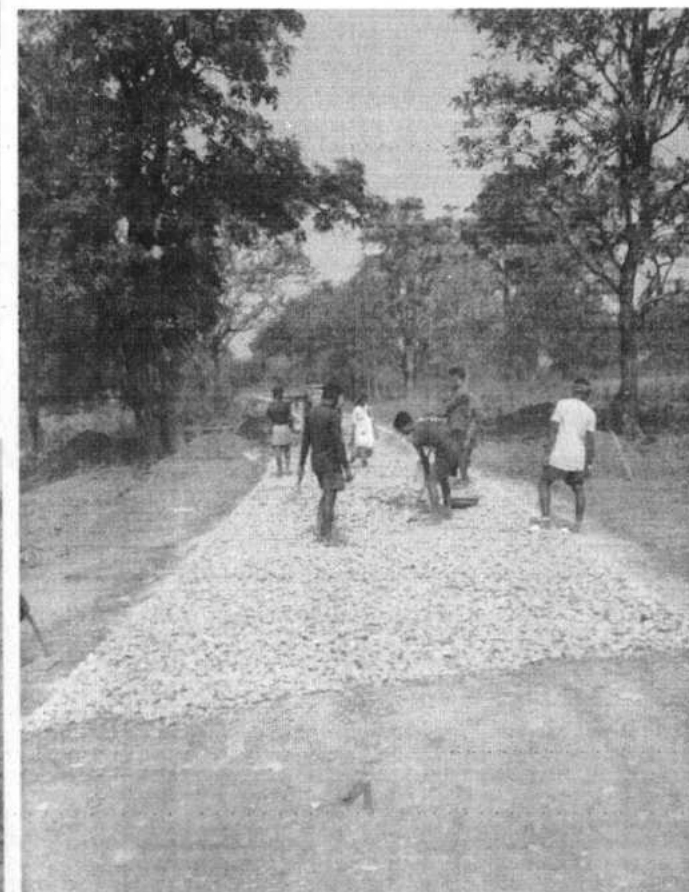

# R.W.S.S Keonjhar and Anandapur Division



## Projects (Major Infra > 5cr) RWSS -Keonjhar

Sl. No	Project name	Sanctioned amount (in cr.)	Released amount (in cr.)	Delayed (in days)
1	Mega PWS scheme to mining affected villages including const. 5 years operation & maintenance cost for 589 villages	709.00 Sanction dt : 19.09.16	601.30 (85% released)	Ongoing (2 years)

## Projects (Major Infra > 5cr) RWSS -Anandapur

1	Mega PWS Scheme of Saharpada Block in 135 villages	219.41 Sanction dt : 14.05.20	187.90 (86% released)	Ongoing (3 Years)
2	Mega PWS Scheme of Ghashipura & Anandapur Block in 200 villages	187.21 Sanction dt : 14.05.20	151.59 (81% released)	Ongoing (3 Years)
3	Mega PWS Scheme of Anandapur Block in 81 villages	135.62 Sanction dt : 14.05.20	115.44 (85% released)	Ongoing (3 Years)

Open Detailed Table

# Hindrances

Open Table

## Abstract of Ongoing / Not started Projects (Major Infra 1cr to 5cr)

Executing department	Total (Ongoing + Not started for projects 1cr to 5cr)	Ongoing	Not started	delayed
EE R& B Keonjhar	33	30	03	12
EE R&B Ghatagoan	30	14	16	13
EE RWD Anandapur	72	66	06	07
EE RWD-I Keonjhar	02	02	00	02
EE RWD-II Keonjhar	52	42	10	41
DFO KJR	03	03	00	00
DFO Apur	02	02	00	00
RWSS APUR	01	01	00	00
RWSS KJR	17	17	00	02
<b>Grand Total</b>	<b>212</b>	<b>177</b>	<b>35</b>	<b>77</b>



## Projects (1cr to 5cr) – Ongoing (Delayed) and Not started

### R&B Keonjhar, Other Projects

SL. No	Name of Project	Sanctioned Amount	Order Letter/Date	Status	Delay
1	Impvt. of road from Bonai Boarder- Barbil- Nalda road to Thakurani via Barbil old stand	3,80,00,000.00	2106/ 07.12.20	On-Going	3 Years
2	Const. of Skill Development Training Centre at Telkoi in the district of Keonjhar for the year 2023-24.	3,60,20,433.00	3194/17.10.23	Not Started	1 Year
3	Special repair to Barbil town road (ODR) from 0/000 K.M. to 3/667 K.M.	1,99,58,000.00	2195/23.11.21	On-Going	2 Years
4	Construction of Approach Road at OAV Bodapalasa, Keonjhar (Such as RCC drain, laying paver block & Hume pipe culvert)	1,15,82,140.00	3530/06.10.22	On-Going	2 Years
5	Const. of E-Type staff quarter at Govt ITI Barbil, Keonjhar	4,40,76,414.00	2885/21.09.23	Not Started	1 Year

### R&B Ghatagaon, Other Projects

1	Transformation of DHH, SDH and other public health facilities via centralized master plan for all essential service (Clinical, Diagnostic, Ancillary & other (Repair & Renovation to Ghatagaon CHC, Ghatagaon under 5T (AMA HOSPITAL)	3,07,35,100.00	1037/15.04.23	On-Going	1 Year
2	Transformation of DHH, SDH and other public health facilities via centralized master plan for all essential service (Clinical, Diagnostic, Ancillary & other (Repair & Renovation to Harichandanpur CHC, Harichandanpur under 5T (AMA HOSPITAL)	3,31,14,300.00	1037/15.04.23	On-Going	1 Year
3	Repair & Renovation work in Govt. ITI, Anandapur at Salapada in the district of Keonjhar.	3,16,34,025.00	3849/04.11.22	On-Going	1 year

Department wise Project Status – R&B Keonjhar and Ghatagaon Projects (1cr to 5cr) Ongoing (Delayed) and Not Started



## DMF Sankalp- Block Level Library

S. No.	Block	Executing agency	A/A Amount (In Cr.)	Released amt. (in Cr.)	Status	Remarks
1	Banspal	R&B Keonjhar	4.47	1.21	First Floor Brick Work	
2	Jhumpura	R&B Keonjhar	4.56	2.65	Roof Level (90%)	
3	Telkoi	R&B Keonjhar	4.62	1.14	First Floor Brick Work	
4	Patna	R&B Ghatagaon	4.46	2.48	Roof Level (90%)	
5	Ghatagaon	R&B Keonjhar	A/A to be done		A/A to be done	
6	Ghasipura	R&B Ghatagaon	4.27	2.98	Completed	
7	Anandapur	R&B Ghatagaon	4.24	2.97	Completed	
8	Hatadihi	R&B Ghatagaon	4.30	3.01	Completed	
9	Harichandanpur	R&B Ghatagaon	4.50	1.35	First Floor Brick Work	
10	Saharpada	R&B Keonjhar	4.48	1.12	First Floor Brick Work	

## RWD Keonjhar -1

SL. No	Name of Project	Sanctioned Amount	Order Letter/Date	Status	Delay
1	Const. of road from NH-215 (Rajabandha) to RD road (Bhaliadihi) via Totasahi	2,48,57,000.00	819/ 11.05.21	On-Going	3 Years
2	Impvt. of road from PWD road Siluan Chhak to NH-49 via Ghutur	2,82,97,000.00	711/30.03.22	On-Going	2 Years

## RWD Keonjhar -2

1	Const. of road from Uperkadakala to Laipani Road	2,23,67,000.00	2473/28.12.21	On-Going	1 Year
2	Const. of road from Uperkadakala to Malartulu road	4,39,95,000.00	2473/28.12.21	On-Going	1 Year
3	Const. of road from Uperkadakala to Mundasahi Road	1,82,67,000.00	2473/28.12.21	On-Going	2 Years
4	Const. of road from Kendughati to Gambharidihi road	2,79,93,000.00	2473/28.12.21	On-Going	2 Years
5	Const. of road from NH-520 to Gandhalpada	2,14,56,000.00	2473/28.12.21	On-Going	2 Years
6	Const. of road & CD works PANGA to PITHAGOLA road	4,28,15,000.00	2473/28.12.21	On-Going	2 Years
7	Const. of road from Khajurimundi to Kumundi	2,74,02,000.00	196/25.01.22	On-Going	1 Year
8	Const. of road from Gonasika to Budhighar	7,33,00,000.00	196/25.01.22	On-Going	1 Year
9	Const. of road from Kalapahada to Soyabali via Raika	7,17,26,000.00	196/25.01.22	On-Going	1 Year
10	Const. of road from NH-520 to Kudarsahi Basti	2,04,51,000.00	196/25.01.22	On-Going	1 Year
11	Const. of road from Kolharoida Dehursahi to "D" Block via raghu Sahi	1,67,57,000.00	196/25.01.22	On-Going	1 Year

**Note:** Most of the Projects have been completed Physically but UC Submission is pending i.e., Portal Data



## RWD Keonjhar -2

SL. No	Name of Project	Sanctioned Amount	Order Letter/Date	Status	Delay
12	Impvt. of road from Satighat to Belda (Mundasahi)	3,69,32,000.00	1115/ 21.08.18	On-Going	4 Years
13	Const. of road from Jajang to Gurubeda	4,53,01,000.00	1115/ 21.08.18	On-Going	4 Years
14	Impvt. Of road from PWD road to Banko	2,52,02,000.00	1115/ 21.08.18	On-Going	5 Years
15	Const. of bridge on the Pandia nallah of Jajang at Gurubeda in the road Jajang to Banspani	1,82,02,000.00	1633/26.11.18, 1952/ 16.11.20	On-Going	3 years
16	impvt. of RD road (Joda Simuli to Patabila)	3,99,95,000.00	1820/16.10.20	On-Going	3 years
17	Kadagadia to Mirigisingha Road	4,28,35,000.00	808/ 07.05.21	On-Going	2 years
18	Const. of road from Sananai-Katulia Sahi	2,08,95,000.00	2473/28.12.21	On-Going	2 years
19	Const. of road from NH-6 to Medinipur (Badaghagara)	4,35,74,000.00	2473/28.12.21	On-Going	2 years
20	Const. of road from PWD road to Balarampur from 0/000 K.M. to 3/100 K.M.	2,83,09,000.00	196/25.01.22	On-Going	1 years
21	Const. of road with culvert from Deojhar Station to Gobardhan pur Naik Sahi	2,29,40,000.00	2435/20.06.22	On-Going	1 year

Department wise Project Status - R.W. Division – I & II, Keonjhar



## RWD Anandapur

SL. No	Name of Project	Sanctioned Amount	Order Letter/Date	Status	Delay
1	Improvement of road from PWD road to Baharipur via Chakundia-Kadamdihi road	1,76,26,763.00	1573/ 13.11.18	On-Going	3 Years
2	Improvement of road from Tukuna to Ambo	2,59,49,076.00	1573/ 13.11.18	On-Going	3 Years
3	Improvement Of road length in 5 K.M. from Maliposi to Sarata	3,61,36,000.00	1783/ 21.12.18	On-Going	2 Years
4	Improvement of road from Barang to Sundarpal	2,18,73,000.00	201/ 20.02.19	On-Going	2 Years
5	Improvement of road from Mahulapankha to Kuradhighasa	1,42,84,000.00	201/ 20.02.19	On-Going	5 Years
6	Improvement of road from Mahulapankha to Kuradhighasa via Junabadi	2,08,81,000.00	201/ 20.02.19	On-Going	5 Years
7	Improvement of road from Mandir Chhak Baliparbat to Haridabadi	1,29,96,000.00	1386/10.08.21	On-Going	2 Years
8	Improvement of road from Dhipasahi to Panchamdumuria	1,49,19,000.00	1386/10.08.21	Not Started	3 Years
9	Improvement of road from Dhenka PWD road Chhak to Jhanajhana road	1,70,00,000.00	866/18.04.22	Not Started	2 Years
10	Const. of road from RD Road to Rajpokharia GP office	1,86,87,000.00	4255/14.12.22	Not Started	2 years
11	Construction of Road Kadakila to Gura Sahi	2,64,19,000.00	889/15.03.24	Not Started	9 Months
12	Construction of Road from RD Road to Sapuakhandi	2,41,34,000.00	889/15.03.24	Not Started	9 Months
13	Construction of Road from Arjunchuha Khadikhaman to Chaturi Sahi	3,23,71,000.00	889/15.03.24	Not Started	9 Months

## Abstract of Unconnected Habitation

Sl No	Block	Road Projects (Nos.)	Length (KM)	A/A Done From DMF	Agreement Drawn	Work in progress	Pending at CE, BBSR office	Remarks
1	Harichandanpur	47	121.5	47	30	26	14	47 projects have been A/A accorded
2	Banspal	19	47.6	15	10	0	08	01 is not feasible & 03 estimates yet to be submitted for A/A
3	Telkoi	20	33.2	20	08	05	12	20 projects have been A/A accorded

Open Detailed Table



# CDM & PHO, Keonjhar

## Health, Welfare of Aged and Disabled

S. No.	Project Name	Issues/Challenges
1	Establishment and Operations of Digital Dispensaries in Keonjhar, Odisha	Out of the 100 sanctioned dispensaries, 34 are yet to become functional.
2	Doctors hiring under DMF	PAR and Agreement status not yet received. Re-assessment of doctors need to be done
3	Thalassemia Diagnosis Machine	Implementation has not yet been initiated.
4	Doctors Online Attendance System	Implementation has not yet been initiated.
5	Medical College & Hospital, Keonjhar	Transfer of DDO power for ministerial staff/paramedics hired through outsourced agency from CDM&PHO to Dean, DDMCH is pending. Additionally, an addendum to the agreement is required to include a third party.
6	Provisioning of support staffs under DPM NHM	2 out of 4 Staffs from DPMU of DSSO (as provided under DMF project contingency head) may be shifted to NHM for support to DPM for M&E of DMF projects

# IDCO



## HMV, Dhanurjaypur, Jhumpura

Sl No	Name of the Project	A/A Amount (in lakhs)	Agreement Amount (in lakhs)	Status	Direction by the Chair to IDCO	Visit Remarks 29-11-2024
3	Providing & Supplying Furniture for Hostel and Academic Block for HMV, Keonjhar	Rs.236.62	<b>Part 1:</b> Rs. 109.67  <b>Part 3:</b> Rs. 16.57  <b>Part 2,4:</b> Agreement yet to be done	<b>Part-1:</b> completed  <b>Part-2:</b> Partially completed (Revised estimate yet to be submitted by IDCO)  <b>Part-3 &amp; 4:</b> Completed	<p>The Chair instructed DH, IDCO to complete the pending activities i.e., Stone pitching (30 m. out of 70 m.) and storm water drainage of 72 m. by 15<sup>th</sup> December 2024.</p> <p>Also, instructed PMU DMF to conduct a field visit to ensure the completion of the above activities adhering to the stipulated deadlines.</p>	<p>CGM, IDCO is yet to analyse the usability as existing storm water drain's capacity far exceeds the water collected in that terrain.</p> <p>(descope: Storm Water Drainage)</p> <p>Response is awaited from CGM, IDCO</p>


# DMF Perspective Plan for next Five Years

- **Identification of Directly and Indirectly affected villages:** Deputy Director of Mines (Keonjhar/ Joda) need to provide the geographic coordinates of mining areas, along with a list of villages and Gram Panchayats (GPs) located within a **15 km radius** from the mines or cluster of mines for directly affected and **25 km radius** from the mines or cluster of mines for Indirectly affected beyond the directly affected area. (as per the revised guidelines of **PMKKKY – Jan 2024**).
- The list of villages may be verified for accuracy by the **Odisha Space Applications Centre (ORSAC)**.
- Utilization of secondary datasets such as **Mission Antyodaya- 2022** and **NFHS-2019** for conducting a gap analysis in the affected regions.
- Conduct of a validation exercise for **10%** of the identified mining-affected villages (approximately **60** villages).
- Identification of gaps across various sectors based on the data analysis. (Power BI Dashboard)
- Formulation of projects to address the identified key gap areas. The respective departments or agencies will be responsible for this task.
- Organizing consultations with key stakeholders to ensure alignment and effectiveness of proposed interventions.

# District Profile

Block, GP, Village	VDI	Tribal Pop Bkt	Blocks	GPs	Villages	Households	Population	ST Population
All	All	All	13	296	2,040	368,027	1,730,357	734,829 (42.5 %)

## Village Development Index

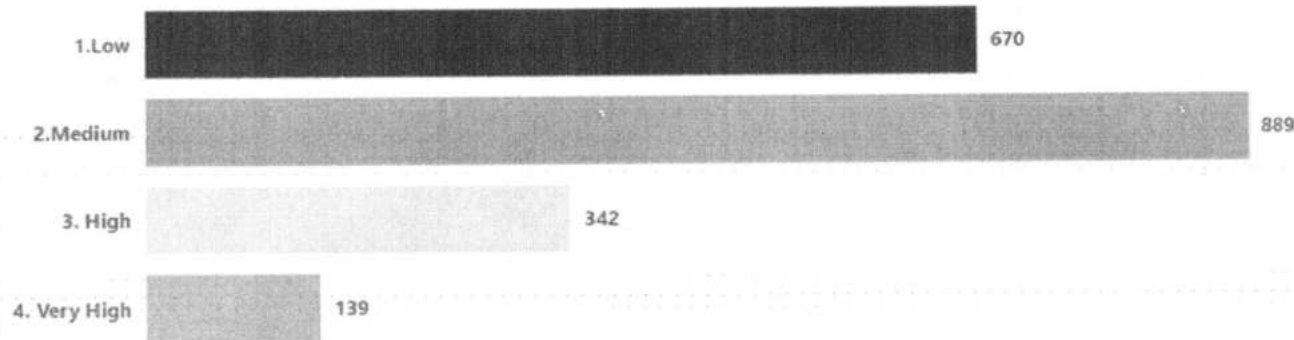

Basic Infra


Health Infra

Education Infra

Financial Infra

Detail Report

## Village Development Index (Choropleth Map)^

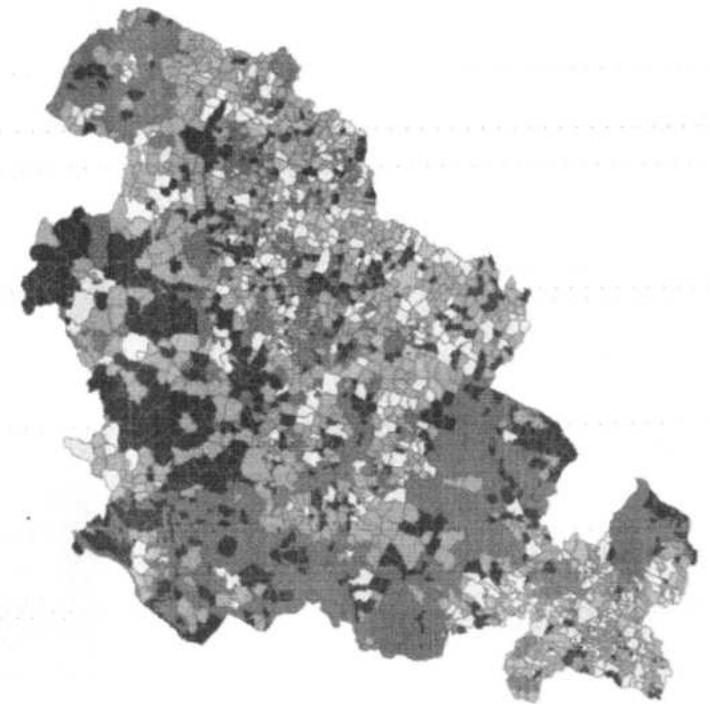

● 1.Low ● 2.Medium ● 3. High ● 4. Very High ● 5.Forest ● 6. Urban Area


\* All the values represent count of villages



# District Profile (Basic Infrastructure)

Block, GP, Village	VDI	Tribal Pop Bkt	Blocks	GPs	Villages	Households	Population	ST Population
All	All	All	13	296	2,040	368,027	1,730,357	734,829 (42.5 %)


Village Development Index



Village Development Index (Choropleth Map)^




Availability of Piped Drinking Water




Village Connected to All Weather Road




Distance from Nearest Piped Drinking Water




Distance from All Weather Road



Availability of Electricity



Villages with Internal CC Road



● 1.Low ● 2.Medium ● 3.High ● 4.Very High ● 5.Forest ● 6.Urban Area


\* All the values represent count of villages




# District Profile (Health Infrastructure)

Block, GP, Village	VDI	Tribal Pop Bkt	Blocks	GPs	Villages	Households	Population	ST Population
All	All	All	13	296	2,040	368,027	1,730,357	734,829 (42.5 %)


Village Development Index




Village Development Index (Choropleth Map)^

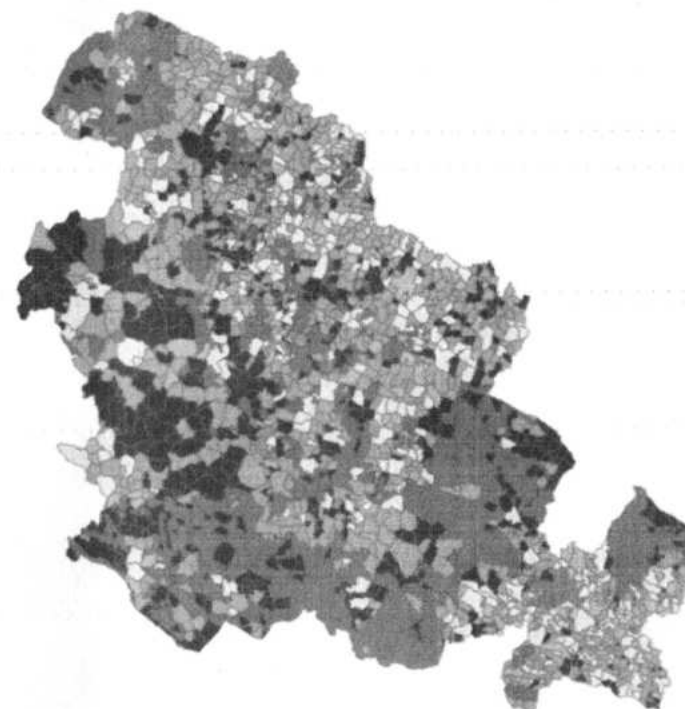


Distance of CHC/PHC

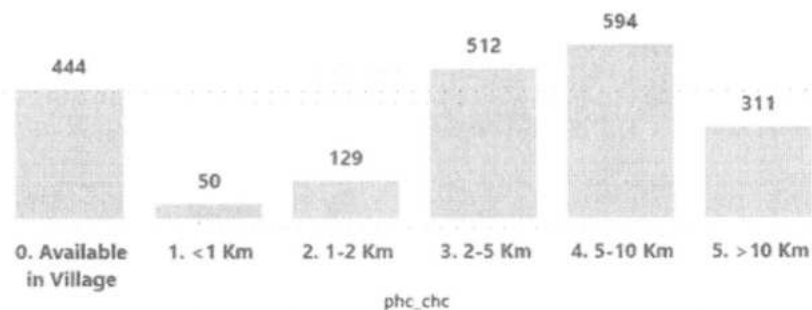

Anganwadi Available




Distance of Anganwadi from Village

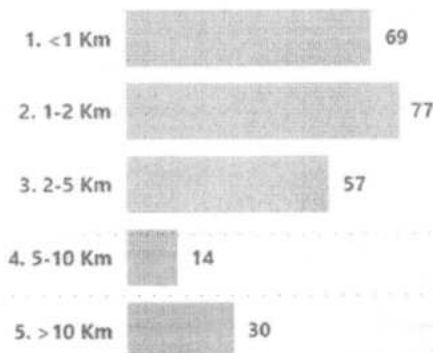

Availability of Mother & Child Facility



Distance of Mother & Child Facility




● 1.Low ● 2.Medium ● 3. High ● 4. Very High ● 5.Forest ● 6. Urban Area

\* All the values represent count of villages

# District Profile (Education Infrastructure)

Block, GP, Village	VDI	Tribal Pop Bkt	Blocks	GPs	Villages	Households	Population	ST Population
All	All	All	13	296	2,040	368,027	1,730,357	734,829 (42.5 %)


Village Development Index




Village Development Index (Choropleth Map)^




Presence of Primary School



Distance of Primary School from Village

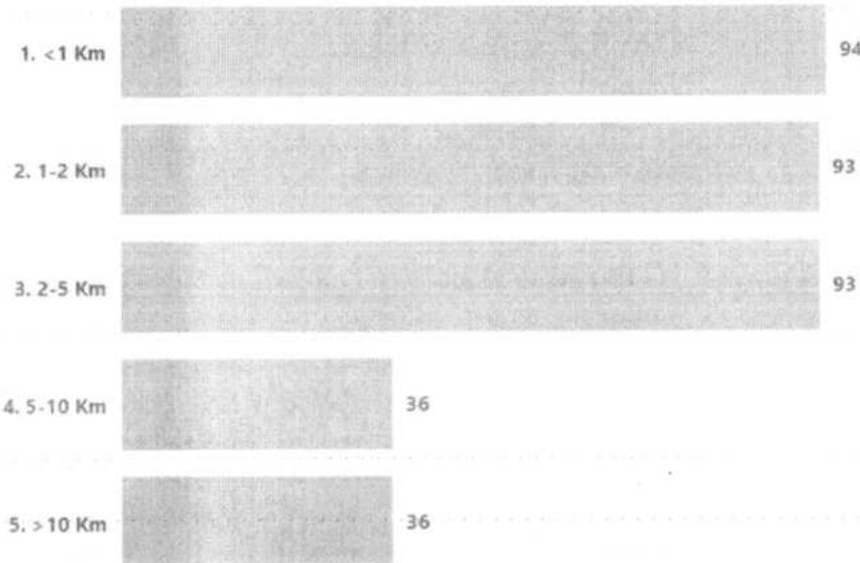

Primary School having Electricity



● 1.Low ● 2.Medium ● 3.High ● 4. Very High ● 5.Forest ● 6. Urban Area


\* All the values represent count of villages




# District Profile (Financial Infrastructure)

Block, GP, Village	VDI	Tribal Pop Bkt	Blocks	GPs	Villages	Households	Population	ST Population
All	All	All	13	296	2,040	368,027	1,730,357	734,829 (42.5 %)


Village Development Index




Village Development Index (Choropleth Map)^

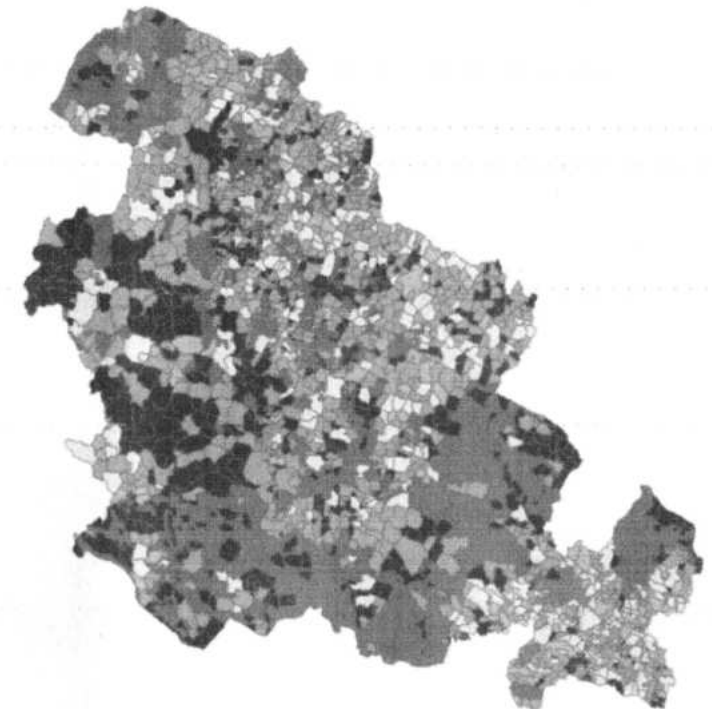

Availability of Bank



Distance of Bank from Village



Availability of ATM




Distance of ATM from Village



Availability of Post Office




Distance of Post Office from Village



● 1.Low ● 2.Medium ● 3. High ● 4. Very High ● 5.Forest ● 6. Urban Area


\* All the values represent count of villages

## Villages without access to Anganwadi centre within 1 km radius vis-à-vis location of creche

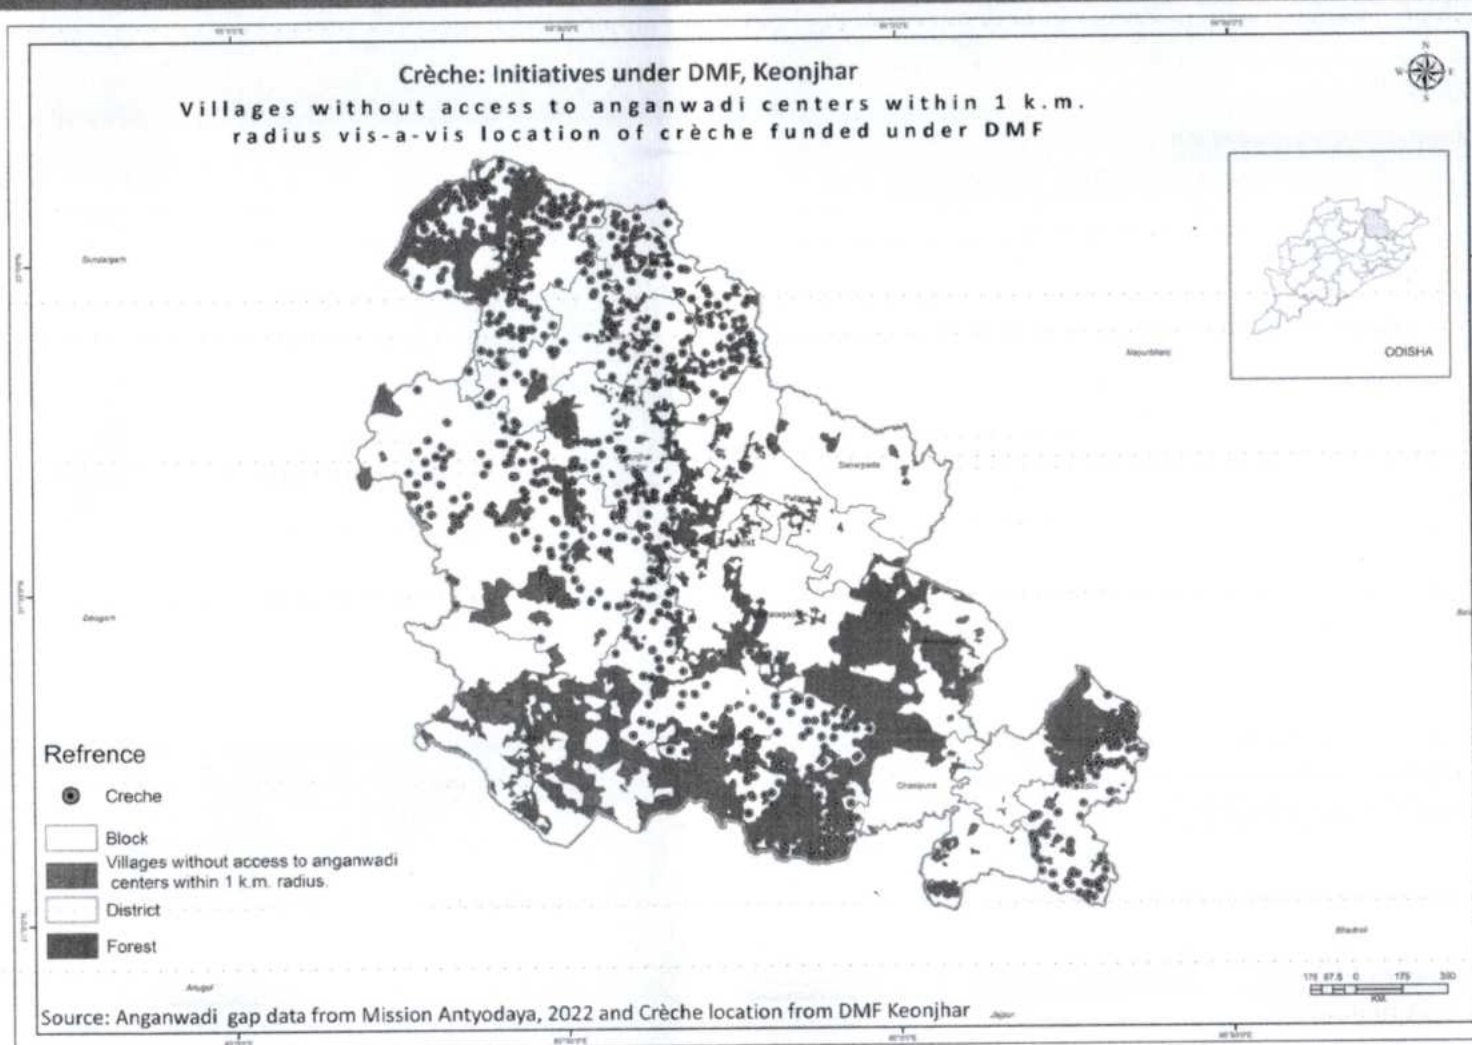

Initiatives under **DMF Keonjhar** to address acute malnutrition among children by providing creches with food and nutrition support, promoting hygiene habits, offering early childhood mental stimulation, and conducting regular growth monitoring.

## Villages without access to CHC/PHC/Sub centre within 10 km radius vis-à-vis location of digital dispensary

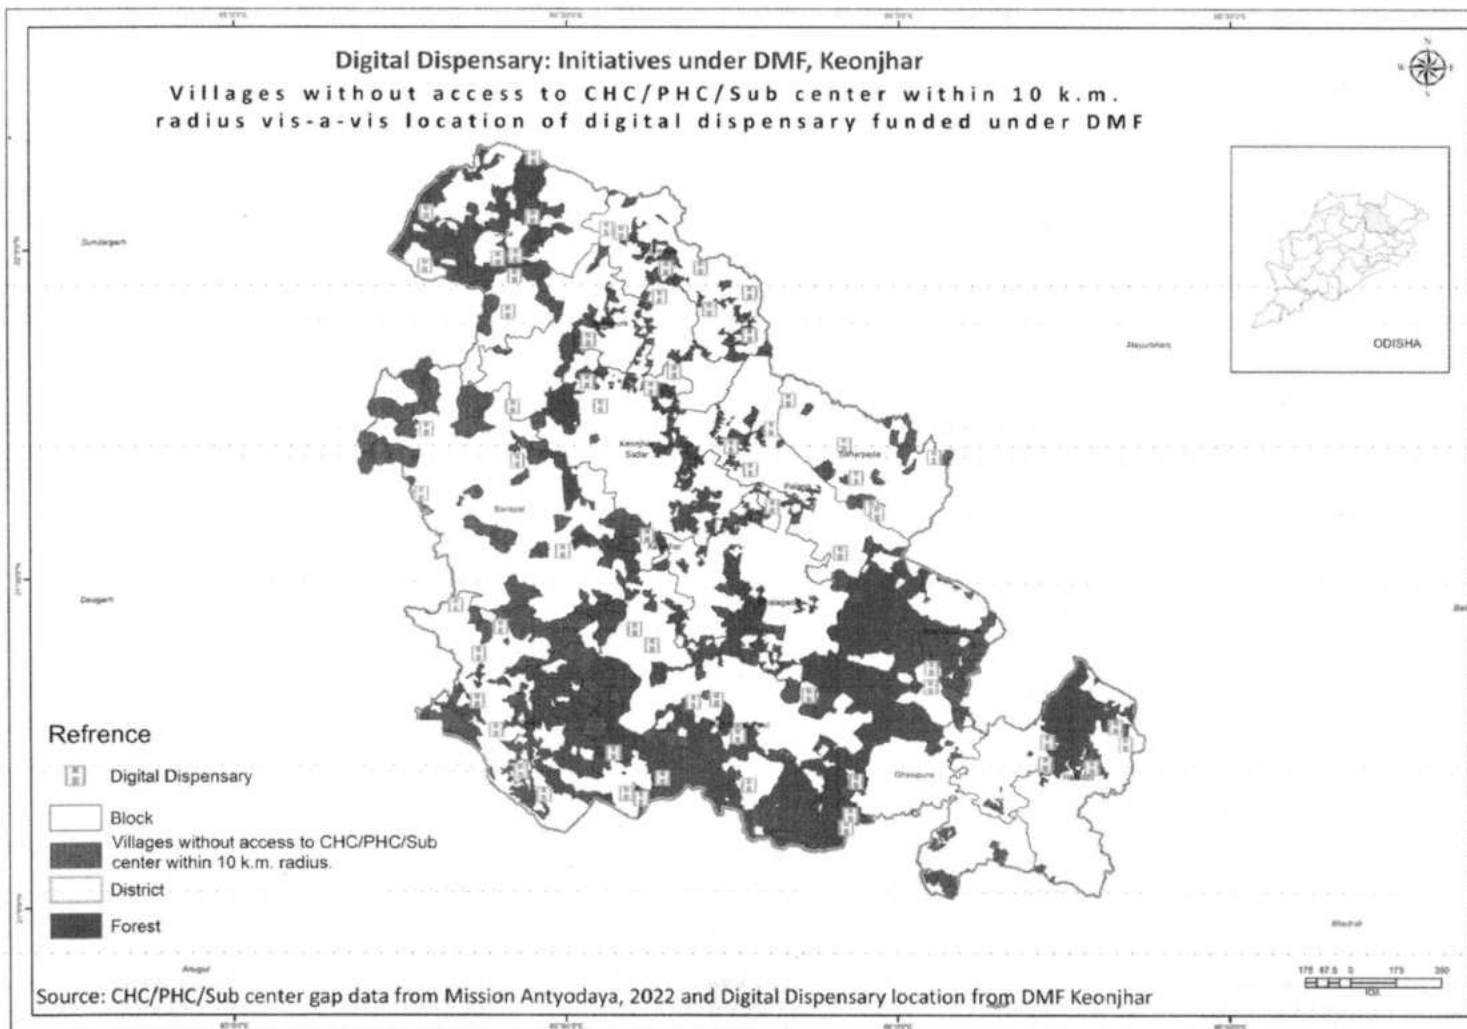

Initiatives under the **DMF Keonjhar** aim to ensure that high-quality healthcare services are provided to people, especially in remote areas where there is a shortage of doctors and other medical staff at the PHC level.



## Audit and Annual Report of DMF

- The Audit report of FY 22-23 has been prepared by the CA and uploaded in the DMF Portal. Post facto approval will be taken in the Upcoming Trust Board.
- The Tax Audit report of FY 23-24 was submitted to IT Department in due time.
- Annual report of FY 22-23 & 23-24 will be approved in the upcoming Trust Board meeting.



## List of Projects to be approved under DMF

Sr. No.	Name of the Project	Block / Municipality	Direct / Indirect Mining	Sector	Executing Agency	Sanction letter no /Date	Post-facto Approval / New	Estimated Budget (in Lakhs)
1	Const. of C.C road from Sapakanta R.D. road to Baditala village.	Banspal	Direct Mining	Infrastructure	BDO Banspal	3924/08.1 1.23	Post-facto Approval	10.00
2	Const. of C.C road from Banspal Gangoda to Goutam house.	Banspal	Direct Mining	Infrastructure	BDO Banspal	3924/08.1 1.23	Post-facto Approval	10.00
3	Const. of culvert from Laxmipur Biswal Sahi to Laxmipur School at Manoharpur, Maharpur GP	Hari.ch.pur	Indirect-mining	Infrastructure	BDO Hari.ch.pur	457/31.01. 24	Post-facto Approval	9.90
4	Const. of CC Road from Mishramal RD Road to Regional High School, Dhanurjaypur-A, Tentalaposi GP	Hari.ch.pur	Indirect-mining	Infrastructure	BDO Hari.ch.pur	457/31.01. 24	Post-facto Approval	8.73
5	Const. of CC Road from Mishramal RD Road to Regional High School, Dhanurjaypur-B, Tentalaposi GP	Hari.ch.pur	Indirect-mining	Infrastructure	BDO Hari.ch.pur	457/31.01. 24	Post-facto Approval	8.73
6	Const. of Guard wall at Achinta Matha, Ranki (Thakurpatna)	Sadar	Direct Mining	Infrastructure	BDO Sadar	3025/06.1 0.23	Post-facto Approval	10.00
7	Const. of CC Road from Raja Munda House to Indumati House at Danuan Villages.	Sadar	Direct Mining	Infrastructure	BDO Sadar	3025/06.1 0.23	Post-facto Approval	10.00
8	Const. of Guard Wall at Tikargumura.	Sadar	Direct Mining	Infrastructure	BDO Sadar	3025/06.1 0.23	Post-facto Approval	10.00



## List of Projects to be approved under DMF

Sr. No.	Name of the Project	Block / Municipality	Direct / Indirect Mining	Sector	Executing Agency	Sanction letter no /Date	Post-facto Approval / New	Estimated Budget (in Lakhs)
9	Const. of CC Road at Raisuan village Tanti Sahi from near Indramani Tanti House to towards main road, Raisuan GP.	Sadar	Direct Mining	Infrastructure	BDO Sadar	3025/06.1 0.23	Post-facto Approval	10.00
10	DMF Scholarship Scheme in Keonjhar Dist. for the eligible student of +2 High Achiever in AHSS exam-2023 (1472 nos. of students)	All	Both	Education	DEO Keonjhar	2530/25.0 8.23	Post-facto Approval	333.00
11	DMF Scholarship Scheme in Keonjhar Dist. for the eligible student of +2 High Achiever in AHSS exam-2023 (1472 nos. of students)	All	Both	Education	DEO Keonjhar	2668/29.1 1.24	Post-facto Approval	276.60
12	Procurement of Truck mounted Water Tanker for WATCO Division, Keonjhar	Keonjhargarh Municipality	Direct Mining	Drinking Water	EE PHD KEONJHAR (GM WATCO)	957/16.03. 24	Post-facto Approval	35.36
13	Construction/Renovation of Boundary and internal approach road at EMRS Ranki	Sadar	Direct Mining	Education	BDO Sadar	-	NEW	60.00
14	Improvement to Ranki Village Main Road under DMF for the year 2023-24.	Sadar	Direct Mining	Infrastructure	EE R&B Keonjhar	4199/06.1 2.23	Post-facto Approval	280.72
15	Const. of open stage inside Anandapur Stadium at Anandapur in the district of Keonjhar for the year 2023-24.	Anandapur Municipality	Indirect-Mining	Infrastructure	EE R&B Ghatagoan	2536/19.0 8.23	Post-facto Approval	5.88



## List of Projects to be approved under DMF

Sr. No.	Name of the Project	Block / Municipality	Direct / Indirect Mining	Sector	Executing Agency	Sanction letter no /Date	Post-facto Approval / New	Estimated Budget (in Lakhs)
16	Construction of solar energy based mini water supply scheme with 3MTR staging galvanized tubular steel structure staing for mounting HDPE water storage tank having capacity 5000 liters at village sarukudar under Banspal Block	Banspal	Direct Mining	Drinking water	EE RWSS Keonjhar	1712/12.0 8.24	Post-facto Approval	5.44
17	Construction of Isolation Room of Old Age Home under Joda Municipality.	Joda Municipality	Direct Mining	Welfare for Aged & Disabled	EO Joda Municipality	2676/29.1 1.24	Post-facto Approval	19.36
18	Construction of Paver road inside south campus of DD University	Keonjhargarh Municipality	Direct Mining	Infrastructure	EO Kjr. Municipality	2740/03.1 2.24	Post-facto Approval	10.77
19	Improvement of CC road in front of Anwasha Hostel.	Keonjhargarh Municipality	Direct Mining	Infrastructure	EO Kjr. Municipality	2740/03.1 2.24	Post-facto Approval	14.31
20	Electrical Power supply & shifting of HT Line from the premises of the Project District Science Centre cum-Planetorium at Ghatagaon. (Installation of 500KVA Transformer, shifting of existing 11 KV 3PH 3 wire overhead line Baigapal & Gadadharpur feeder into XLPE insulated cable.	Ghatagaon	Indirect-Mining	Education	S.E.(Elect.), TPNODL, Keonjhar	4117/01.1 2.23; 36/11.01.2 4	Post-facto Approval	102.30



## List of Projects to be approved under DMF

Sr. No.	Name of the Project	Block / Municipality	Direct / Indirect Mining	Sector	Executing Agency	Sanction letter no /Date	Post-facto Approval / New	Estimated Budget (in Lakhs)
21	Construction of Hume Pipe Culvert, Laying of Paver Block & Spreading Moorum from NH to Bhagamunda Market Area at Bhagamunda under Harichandanpur Block.	Hari.ch.pur	Indirect-mining	Infrastructure	PA ITDA Keonjhar	2387/10.08.23	Post-facto Approval	17.40
22	Const. of Drinking water point & Approach road to Community Toilet, Deep Borewell with water supply at Bhagamunda Market Area under Harichandanpur Block.	Hari.ch.pur	Indirect-mining	Infrastructure	PA ITDA Keonjhar	4040/24.11.23	Post-facto Approval	18.00
23	Provisioning of necessary educational infrastructure (Furniture) for South Campus of DD University	Sadar	Direct Mining	Education	R&B Keonjhar	-	NEW	600.00
24	Improvement to road from "Karrow Bridge to Tanto via lotapani" under DMF(PART 2)Revised part.	Joda	Direct Mining	Physical Infra	RWD -II KJR	320/31.01.2023	Deviation	305.93
25	Improvement to road from "Juruli to Bichhakundi via khandabandha" under DMF(PART 2)Revised part.	Joda	Direct Mining	Physical Infra	RWD -II KJR	320/31.01.2023	Deviation	368.45
26	Improvement to road from "Dubuna pidhapokharii" under DMF(PART 2)Revised part.	Joda	Direct Mining	Physical Infra	RWD -II KJR	23/09.01.2018	Deviation	347.51

List of Projects to be approved under DMF

44



## List of Projects to be approved under DMF

Sr. No.	Name of the Project	Block / Municipality	Direct / Indirect Mining	Sector	Executing Agency	Sanction letter no /Date	Post-facto Approval / New	Estimated Budget (in Lakhs)
27	Renovation of existing building canteen shed, E-corner & compound wall at DD University.	Keonjhargarh	Both	Physical Infra	R&B KJR	2963/24.1 2.24	Post-facto Approval	27.63
28	Construction of road from back side south campus to establish easy connectivity between University and Old Town.	Keonjhargarh	Both	Physical Infra	R&B KJR		NEW	76.72
29	Construction of MS Grill Baricade and both side Divider at entrance of south campus DD University.	Keonjhargarh	Both	Physical Infra	E.O KJR		Post-facto Approval	14.92
30	Construction of Boundary Wall & Gate of Janghira UGME School.	Harichandan pur	Indirect Mining	Education	BDO Harichandanpur	952/16.03. 2024	Post-Facto Approval	10.00
31	Renovation/Upgradation of Hostels in Keonjhar District (19 Proposals)	Champua	Direct Mining	Education	PA ITDA Champua	467/31.01. 2024	Post-Facto Approval	146.68
32	Rejuvenation and Restoration of Badabandha Pokhari	Jhumpura	Indirect Mining	Env. Preservation & Pollution Control Measures	PD Watershed/BDO Jhumpura		Post-Facto Approval	950.00
33	Renumeration of Group C & D Staffs in DMF Office (Oct. 2017 to March 2025)	-	-	-	-	-	Post-Facto Approval	85.00

List of Projects to be approved under DMF	45
---	----

45



## List of Projects to be approved under DMF

[illegible]

Collector-cum-Managing Trustee  
D.M.F., Keonjhar

Thank You



## District Mineral Foundation, Keonjhar

Attendance Sheet DMF <u>EE Meeting (31.12.2024)</u>				
Taken Up By <u>Collector cum Chairperson, DMF, Keonjhar</u>				
Date <u>31.12.2024</u> Time <u>11:00 AM</u>				
Venue <u>Zilla Parishad Conference hall (DMF, Keonjhar)</u>				
Sl. No.	Name	Designation	Contact Number	Signature
1	Shri Vishal Singh	Collector, Keonjhar		<i>[Signature]</i>
2	Shri Dharmajit H.D. (IFS)	DFO, Keonjhar	9437055315	<i>[Signature]</i>
3				
4	Abhay Ku. Dahi	DFO, Keonjhar M.	9437096829	<i>[Signature]</i>
5	BINOD BEHARI DA	Advt. Chief	9437639261	<i>[Signature]</i>
6		RWB-I, Keon		<i>[Signature]</i>
7	Harekrishna Panda	EE Ghataggon	9437146566	<i>[Signature]</i>
8	Ashok Kumar Majhi	EE RWD-2, Keonjhar	9437255362	<i>[Signature]</i>
9	Hemanta Ku Sethi	A.E.E, RWD, Keonjhar II	7609960398	<i>[Signature]</i>
10	Ganeswar Nayak	D.S.DFO Keonjhar	7978693393	<i>[Signature]</i>
11	Abhisek Chakrab	CMCDF, Keonjhar	789479086	<i>[Signature]</i>
12	Bishupada Red	DDM, Keonjhar	9937125241	<i>[Signature]</i>
13	Dinesh Agrawalla	DDM, Joda	9438918217	<i>[Signature]</i>
14	Sarat Kumar Giri	L.A.O (A)	9348126559	<i>[Signature]</i>
15	Kamratan Nanda	A.E.E R.W. Div <sup>n</sup> Anandpur	9438989849	<i>[Signature]</i>
16	Basanta Kumar Behera	JE, RW Division	8144145269	<i>[Signature]</i>
17	Pratap Ch. Behera	EE RWD, Anandpur	9778103550	<i>[Signature]</i>
18	Mans Raju Panda	EE RWD, Anandpur	94397554	<i>[Signature]</i>
19	Kamrunnisa Jari	A.E. RWD-D, Anandpur	8895996505	<i>[Signature]</i>
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
